

1. **Mini Basins BC-2A, 2B, 2C and 5B Sewer System Improvements Project**

- **Project Location:** Eastern Linglestown Area – [Map](#)
- **Contract Work:** Replacement Storm and Sanitary Sewer System
 - Sanitary** – 7.5 miles of mainline sewer, 190 manholes, 530 laterals
 - Storm** – 2.0 miles, 125 structures
- **Contractor:** DOLI Construction Corporation
- **Contract Value:** \$17,086,054.25
- **Contract Value Paid to Date:** \$17,184,673.61 (*Final*)
- **Approximate Percent Complete:** 100%
- **Substantial Completion Date:** September 18, 2021
- **Final Completion Date:** November 18, 2021
- **Project Status:**
 - Final adjusting change order approved at June 20, 2023 BOS meeting and all project closeout documents executed by contractor.

2. **Concrete Curb and Sidewalk Replacement**

- **Contract Work:** Replacement of concrete curb and sidewalk as needed
- **Contractor:** Rogele, Inc.
- **Contract Value:** \$612,050.00
- **Contract Value Paid to Date:** \$102,265.76 (*through April*)
- **Approximate Percent Complete:** 16%
- **Project Status:**
 - No work orders issued in last reporting period.

3. **2020/2021 Lining Project**

- **Project Location:** Twin Lakes/Union Deposit Rd and portions of Eastern Linglestown (Blue Ridge Ave, Rockford Heights, Englewood Heights, Balthaser, Collington Ct, etc.)
- **Contract Work:** Lining of Storm and Sanitary Sewer System
 - Sanitary** – 4.0 miles of mainline sewer, 120 manholes, 200 laterals
 - Storm** – 0.3 miles
- **Contractor:** Granite Inliner, LLC
- **Subcontractors:**
 - Lateral Lining – Musson Brothers Inc
 - Manhole Lining – Marra Services Inc.
- **Contract Value:** \$3,074,388.50
- **Contract Value Paid to Date:** \$2,471,544.57 (*through February*)
- **Approximate Percent Complete:** 80%
- **Substantial Completion Date:** August 12, 2022
- **Final Completion Date:** August 31, 2022
- **Project Status:**
 - Change Order #1, time extension, approved at June 7, 2022 Board of Supervisors meeting.
 - The majority of Punchlist items were completed through April 2023.

- Staff currently working with contractor to complete contract closeout.

4. **Mini Basins BC-7A, 7B, 7C, 7D and 8C Sewer System Improvements Project**

- **Project Location:** Devonshire and Southern Paxtonia Areas – [Map](#)
- **Contract Work:** Replacement or Rehabilitation Storm and Sanitary Sewer System
 - **Sanitary** – 6.6 miles of mainline sewer, 205 manholes, 596 laterals
- **Contractor:** DOLI Construction Corporation
- **Contract Value:** \$18,886,489.20
- **Contract Value Paid to Date:** \$8,341,832.17 (*through July*)
- **Approximate Percent Complete:** 44.2%
- **Substantial Completion Date:** August 1, 2024
- **Final Completion Date:** October 1, 2024
- **Project Status:**
 - Fairmont Drive Box Culvert replacement completed and opened.
 - (1) Additional short-term closures will be needed to complete final Wearing Course
 - Pipe replacement completed, restoration and punch list items remain:
 - (1) Work Zone #10
 - (2) Work Zone #9
 - (3) Work Zone #3
 - (4) Work Zone #2
 - (5) Work Zone #1
 - Work continuing in:
 - (1) Work Zone #4
 - (2) Work Zone #7
- **Items to Note:**
 - Upcoming work:
 - (1) Continuing concrete and lawn restoration in Work Zones South of Devonshire Heights Road
 - (2) Final Wearing Course placement in Work Zones South of Devonshire Heights Road

5. **Township Construction Crew**

- **Project Location:** Devonshire and Southern Paxtonia Areas (BC-7/8) – [Map](#)
- **Approximate Percent Complete:** 64%
- **Project Status:**
 - Following work areas remain in project area.
 - (1) Burgundy Rd (Site #8a) – Approximately 87% Completed
 - (a) Remainder of work to be completed concurrently with Sanitary mainline.
 - (2) Meadowbrook Dr and Oak Ave (Site #2) – 80% complete, remainder of work to be completed during next reporting period.
 - (3) Kenwood Ave and Glenwood Ave (Site #4) – Work to be completed upon completion of Sanitary mainline.
 - (4) Devonshire Heights Rd (Site #7) – Work to be completed after utility relocations.
 - (5) Tyler Dr (Site #8b)

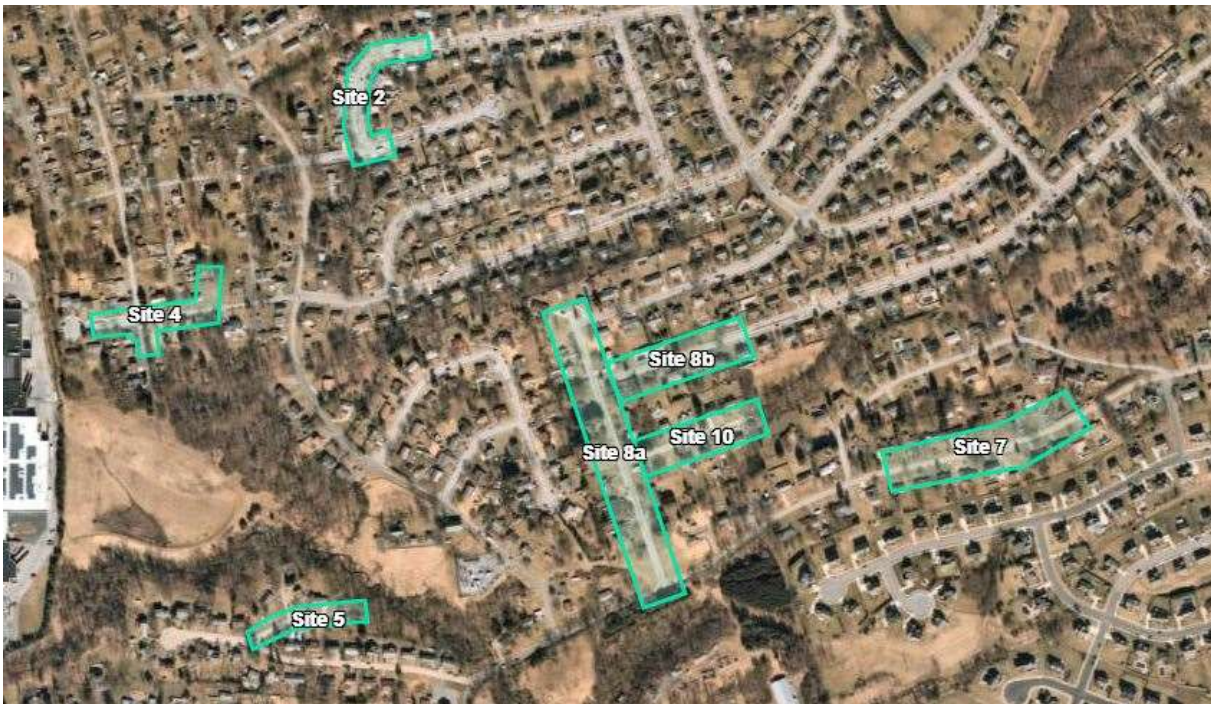


Figure 1: Township Storm Sewer Replacement Crew Work Areas - North



Figure 2: Township Storm Sewer Replacement Crew Work Areas - South

- **Upcoming Work:**
 - M Street Storm Sewer Replacement
 - 2024 LPT Street Paving Repairs
